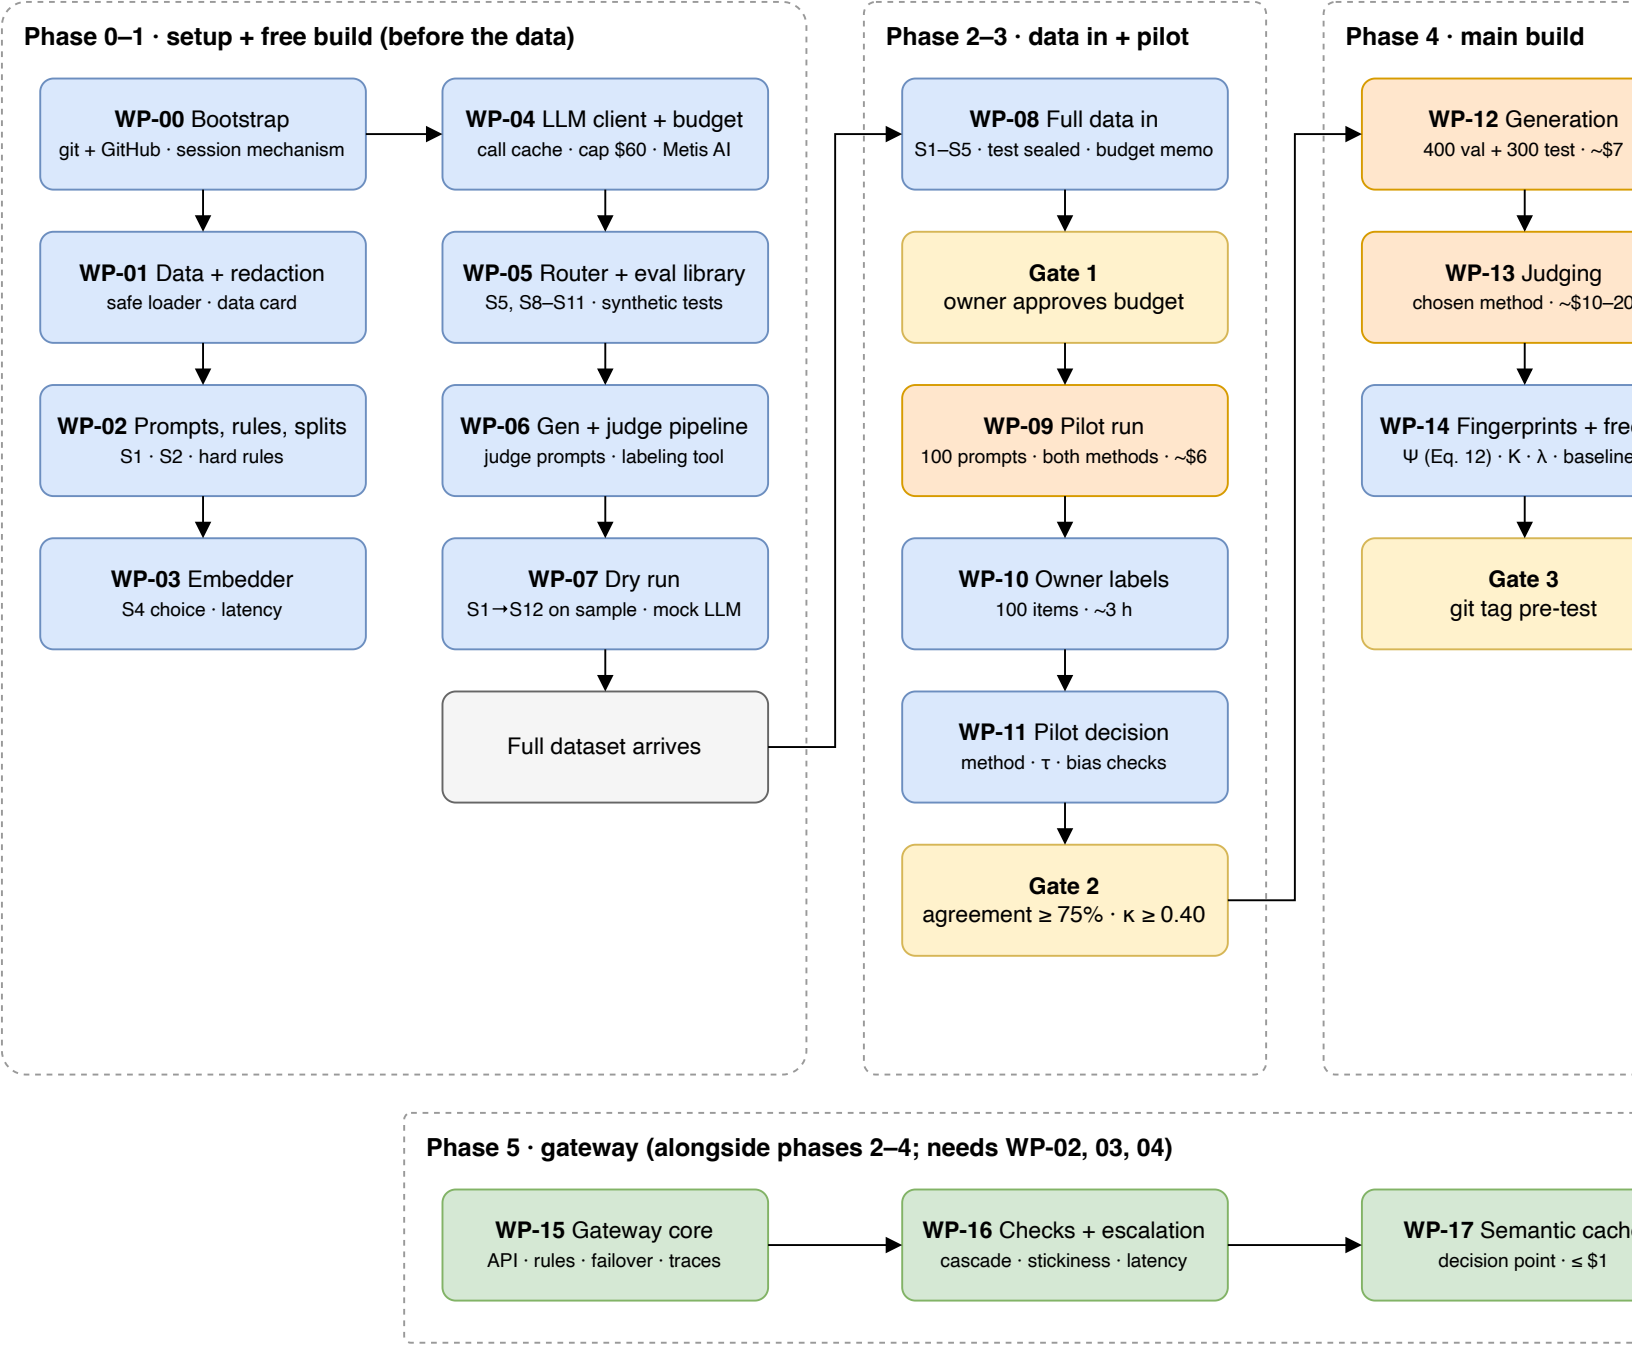
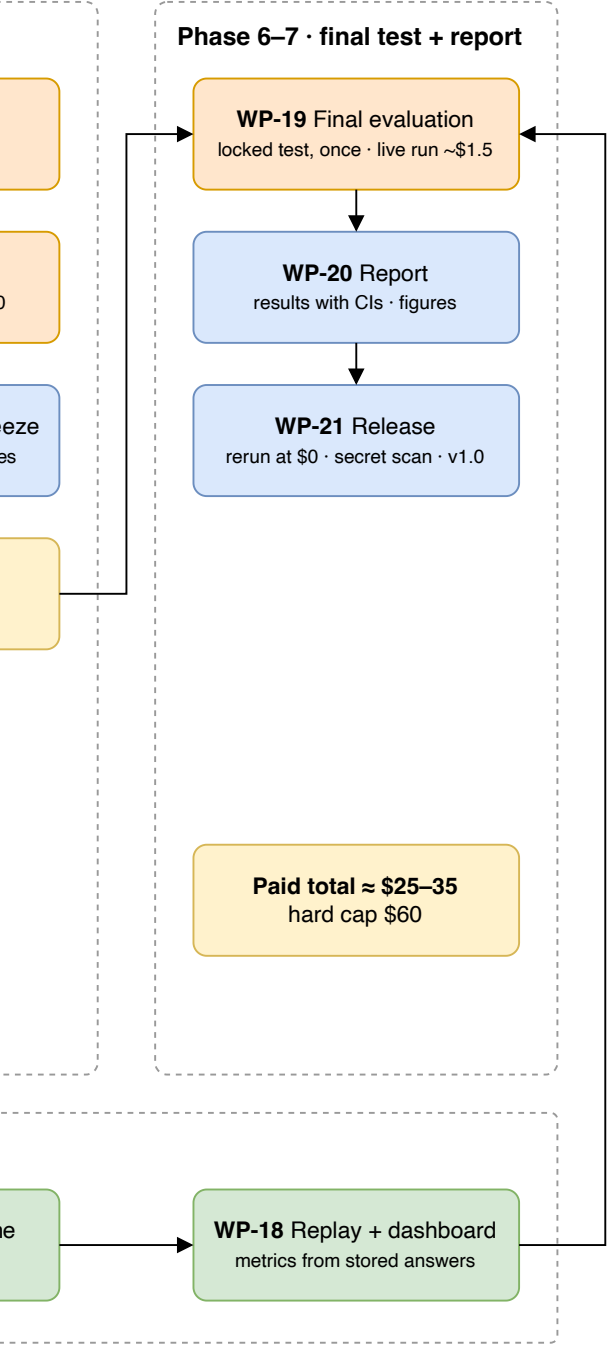

Phase 0–1 · setup + free build (before the data)
WP-00 Bootstrap
git + GitHub · session mechanism
WP-01 Data + redaction
safe loader · data card
WP-02 Prompts, rules, splits
S1 · S2 · hard rules
WP-03 Embedder
S4 choice · latency
WP-04 LLM client + budget
call cache · cap $60 · Metis AI
WP-05 Router + eval library
S5, S8–S11 · synthetic tests
WP-06 Gen + judge pipeline
judge prompts · labeling tool
WP-07 Dry run
S1→S12 on sample · mock LLM
Full dataset arrives
Phase 2–3 · data in + pilot
WP-08 Full data in
S1–S5 · test sealed · budget memo
Gate 1
owner approves budget
WP-09 Pilot run
100 prompts · both methods · ~$6
WP-10 Owner labels
100 items · ~3 h
WP-11 Pilot decision
method · τ · bias checks
Gate 2
agreement ≥ 75% · κ ≥ 0.40
Phase 4 · main build
WP-12 Generation
400 val + 300 test · ~$7
WP-13 Judging
chosen method · ~$10–20
WP-14 Fingerprints + fre
Ψ (Eq. 12) · K · λ · baseline
Gate 3
git tag pre-test

Phase 5 · gateway (alongside phases 2–4; needs WP-02, 03, 04)
WP-15 Gateway core
API · rules · failover · traces
WP-16 Checks + escalation
cascade · stickiness · latency
WP-17 Semantic cach
decision point · ≤ $1


Phase 6–7 · final test + report
WP-19 Final evaluation
locked test, once · live run ~$1.5
WP-20 Report
results with CIs · figures
WP-21 Release
rerun at $0 · secret scan · v1.0
Paid total ≈ $25–35
hard cap $60
WP-18 Replay + dashboard
metrics from stored answers
